

Winnetka Campus East Side Academic and Athletic Project Community Meeting

April 2022

NEW
TRIER



Agenda

1. Current Progress
2. Schedule
3. Upcoming Work






Main Gym - 2nd Floor



Indoor Track / Practice Field - Lower Level

Site Plan

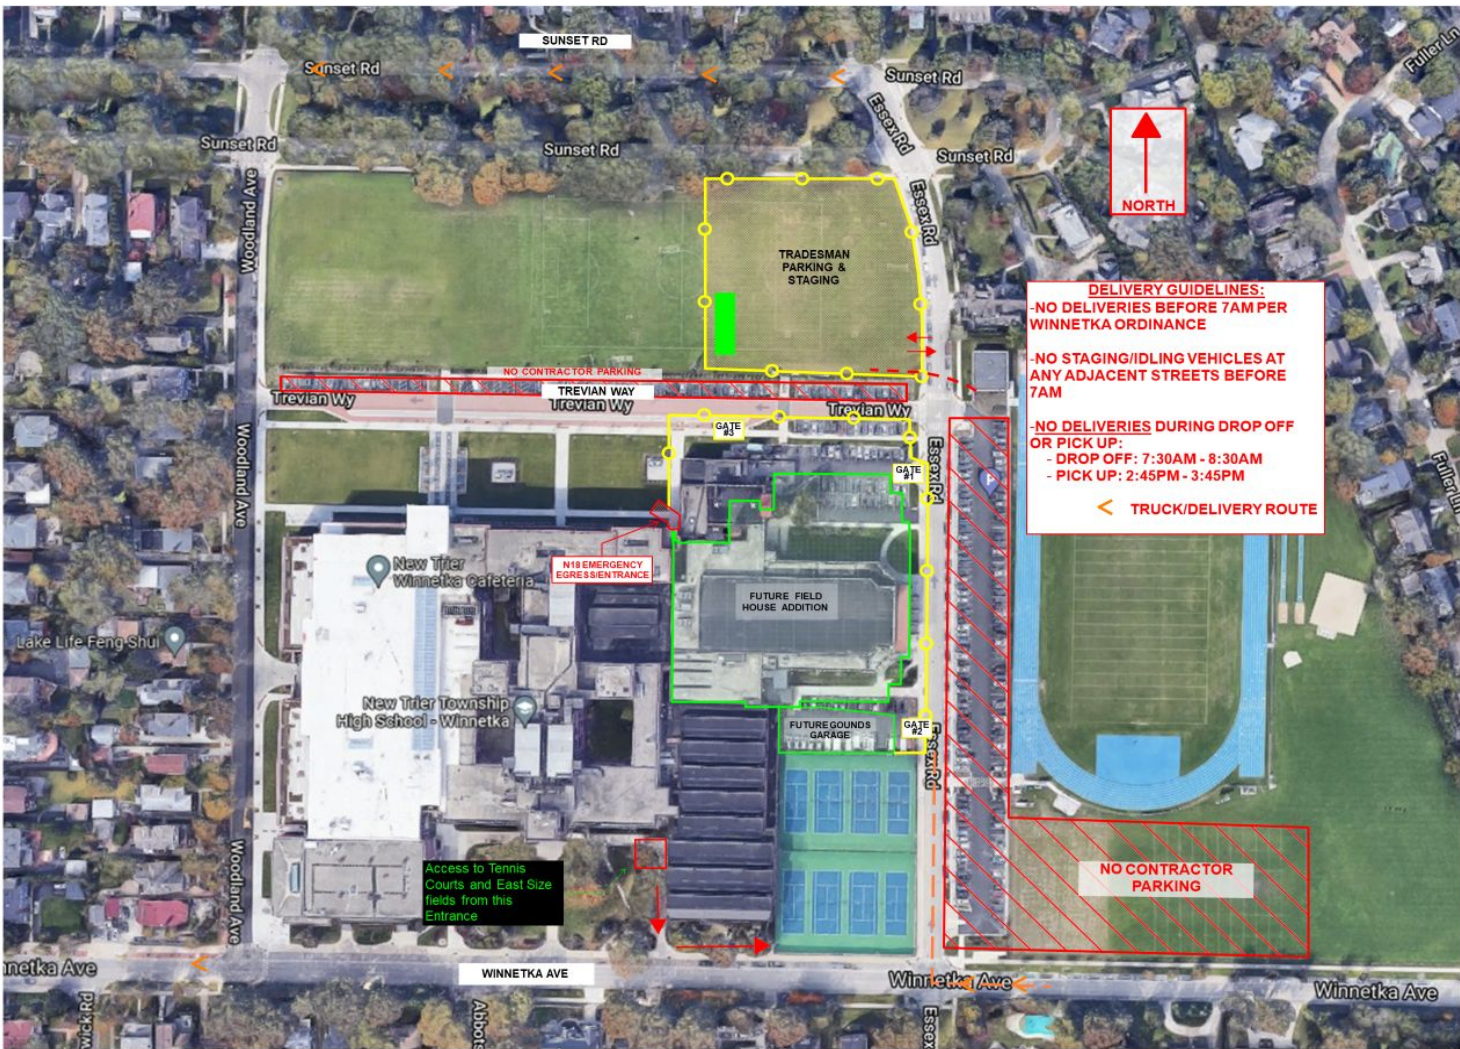

DELIVERY GUIDELINES:
 -NO DELIVERIES BEFORE 7AM PER WINNETKA ORDINANCE
 -NO STAGING/IDLING VEHICLES AT ANY ADJACENT STREETS BEFORE 7AM
 -NO DELIVERIES DURING DROP OFF OR PICK UP:
 - DROP OFF: 7:30AM - 8:30AM
 - PICK UP: 2:45PM - 3:45PM
 < TRUCK/DELIVERY ROUTE



Current Construction Progress

- Major demolition activities completed
- Mass excavation has concluded; foundation specific excavation activities continue
- Concrete contractor on site placing footings and foundation walls



Current Construction Progress



Current Construction Progress







Upcoming Project Phases


- Upcoming schedule
 - Mass Excavation Complete, additional activities continue for concrete work
 - Concrete Work in progress, Footings and Foundation Walls
 - Steel Work Starting Week of April 25th and Crane Mobilization
 - Mechanical, Electrical and Plumbing trades on site coordinating installation activities with concrete work

New Trier Winnetka Campus East Side Academic and Athletic Project																																							
CONSTRUCTION SCHEDULE																																							
Tuesday, April 19, 2022																																							
				2021-2022 Academic Year												Summer						2022-2023 Academic Year						Summer						2023-2024					
				2021						2022						2023						2024																	
Line	Activity	Start	Finish	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12						
CONSTRUCTION																																							
10	Mobilization	11/29/2021	12/31/2021																																				
11	Site Removals	12/21/2021	01/20/2022																																				
12	Abatement and Demolition	12/20/2021	02/16/2022																																				
13	Excavation	02/14/2022	04/30/2022																																				
14	Structure (concrete/steel)	03/10/2022	07/26/2022																																				
15	Exterior Façade	06/01/2022	09/30/2022																																				
16	Interior Construction	06/01/2022	06/01/2023																																				
17	Site Utilities	07/27/2022	08/18/2022																																				
18	Site Paving and Landscaping	04/15/2023	05/31/2023																																				
19	Substantial Completion	06/01/2023																																					
20	Owner Move In	06/01/2023	07/15/2023																																				
21	Final Completion	07/31/2023																																					
22	First Day of School (est.)	08/21/2023																																					
23																																							
24																																							



Upcoming Project Phases

- Structural Steel Mobilizing and beginning the last week of April.

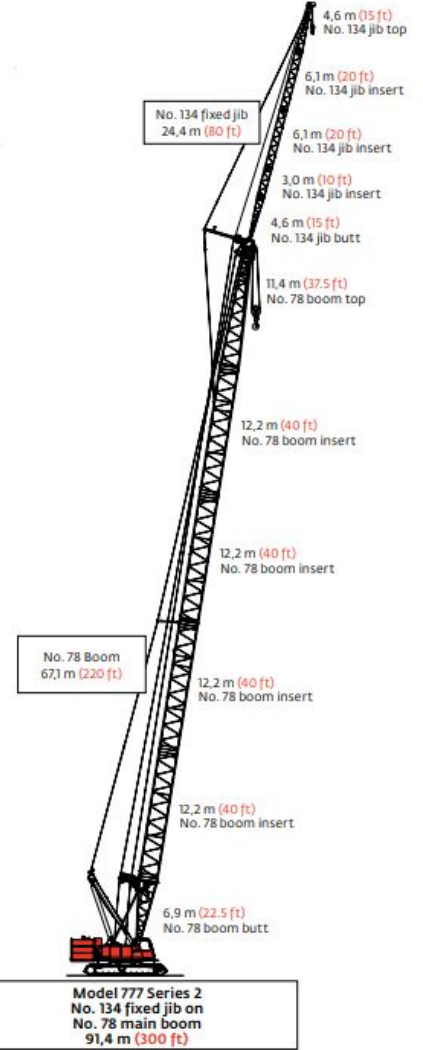


Neighbor Liaison

Niki Dizon
Director of Communications

(847) 784-2666

dizonn@nth.s.net

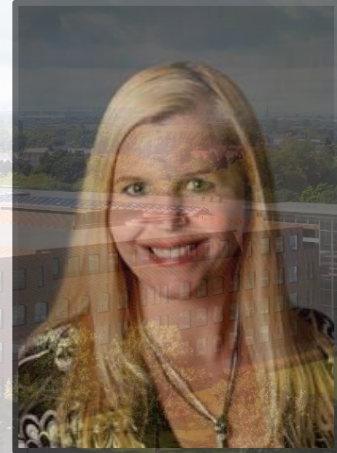

Questions

Thank you for attending! We appreciate your questions, patience and understanding as we work to prepare New Trier for the next generation of students

